Customer Ready Date: Aug 17, 2020

Minnesota Energy Resources

Field Site Visit: (•) Service Card ( ) Main Card

WR: 3060194

Related WR: 3098547

Customer Name:

Address: 19760 Grouse Rd

Cross Street: 200th St

City: Little Falls Within City Limits? No

Premise #:

Contact Number:

County: Morrison

Taxing District: 256

Main Size: **2"** *PSI: **115** Material: **Steel** CP: **Rectifier**

* If Service PSI is greater than 60#, please refer to Engineering

Job Type: GS Type of Service: Residential Location: Short Side

Svc Requires Main? No

Additional Information / Special Instructions / Contacts / Directions / Notes:

See related WR for main installation

This service will require a first cut at the ROW, so will need to trench 25' of 3/4" steel from 2" steel main to the edge of ROW (plus a 4-post barricade with cross-members)

From the first cut, plow 1" PE 218' to edge of groomed yard; from that point, directional bore the remaining 178' to desired meter location on north side of home

Service to be inserted in gopher guard

Install EFV on service

Will need a 250 meter and 2# meter bar

Permits Required
(Check all that apply)

- [ ] Township
- [ ] City
- [x] County
- [ ] MnDOT
- [ ] Environmental?

Please refer to EPREP for more information.

Pipe Install: Material: MDPE

Quantity (ft): 396' Size (in): 1"

Retire: [ ] CWS [ ] Xtrube [ ] Copper

Add. Bellhole [ ] BS [ ] MDPE [ ] Aldyl-A

Quantity (ft): Size (in):

Check All That Apply: [ ] Curb Value [ ] Meter Remove [ ] Mtr Bar Remove

[x] Regulator [x] EFV [x] Meter Bracket [x] Reg Ice Shield

[ ] Barricade [x] Riser [x] Meter Bar [ ] Mtr Ice Shield

Meter Set needed? Yes Multiple Meters? No

Size: 250 PSI: 2 Quantity

Excavation (sq ft unless otherwise stated)		**Restoration** (sq ft unless otherwise stated)	
Dir.Bore (lin ft): 103	Conv.Bore (lin ft):	Sod:	BD&S: 150
Concrete:	Blacktop:	Gravel (cu yds):	Sand:
Sawing (lin ft):		C&G (lin ft):	Tamping:
Rock Peel (cu yd):	Rock Haul (cu yd):	Concrete:	Blacktop:
Plow: 293'			

Customer UG Facilities? Type of UG Facilities:

Excess Footage: 321' P/L to Meter: 396' Estimate: $2,472.81

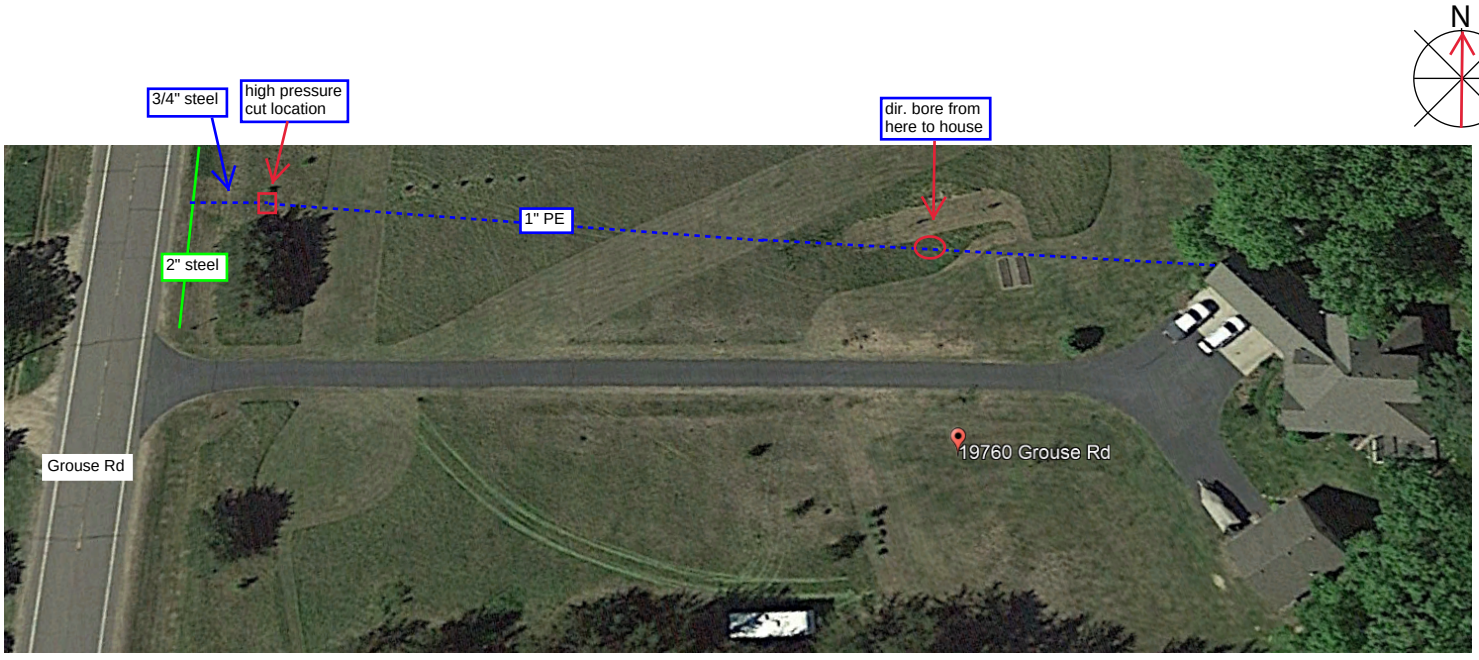

Technician Name: Tricia Montbriand Telephone: +1 (320) 980-6382 Date: 7-23-20

Form Revision Date: 8-22-2017

Reset Form | Check Spelling | Print Form | Submit by Email | Save As
